

Appendix Y


Proponents Construction Program

ID	Task Mode	Task Name	Duration	Start	Finish	Timeline											
						Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026				
1		HPS2 CONSTRUCTION PHASE	856 days	Mon 3/04/23	Mon 13/07/26	[Timeline bar]											
2		TCW00419 PIPELINE INSTALLATION	757 days	Mon 3/04/23	Tue 24/02/26	[Timeline bar]											
3		Possession of site	0 days	Mon 3/04/23	Mon 3/04/23	[Timeline bar]											
4		Site mobilisation and establishment	30 days	Mon 3/04/23	Fri 12/05/23	[Timeline bar]											
5		Pipeline Construction Section 1 - Pumpstation to VP2	280 days	Mon 15/05/23	Fri 7/06/24	[Timeline bar]											
6		Clearing and grubbing	35 days	Mon 15/05/23	Fri 30/06/23	[Timeline bar]											
7		Access track construction	30 days	Mon 3/07/23	Fri 11/08/23	[Timeline bar]											
8		Dig, lay and backfill pipe	90 days	Mon 14/08/23	Fri 15/12/23	[Timeline bar]											
9		VP1 construction	65 days	Mon 14/08/23	Fri 10/11/23	[Timeline bar]											
10		TB1 construction	65 days	Mon 4/09/23	Fri 1/12/23	[Timeline bar]											
11		VP2 construction	65 days	Mon 25/09/23	Fri 22/12/23	[Timeline bar]											
12		Rehabilitation	80 days	Mon 11/09/23	Fri 29/12/23	[Timeline bar]											
13		Hydrostatic testing	20 days	Mon 1/01/24	Fri 26/01/24	[Timeline bar]											
14		Pipeline appurtenances and valve pit fit out	65 days	Mon 29/01/24	Fri 26/04/24	[Timeline bar]											
15		Removal of stockpile yards and temporary access roads	65 days	Mon 29/01/24	Fri 26/04/24	[Timeline bar]											
16		Final rehabilitation	30 days	Mon 29/04/24	Fri 7/06/24	[Timeline bar]											
17		Pipeline Construction Section 2 - VP2 to VP3	310 days	Mon 22/05/23	Fri 26/07/24	[Timeline bar]											
18		Clearing and grubbing	45 days	Mon 22/05/23	Fri 21/07/23	[Timeline bar]											
19		Access track construction	45 days	Mon 24/07/23	Fri 22/09/23	[Timeline bar]											
20		Dig, lay and backfill pipe	105 days	Mon 25/09/23	Fri 16/02/24	[Timeline bar]											
21		TB2 construction	65 days	Mon 25/09/23	Fri 22/12/23	[Timeline bar]											
22		TB3 construction	65 days	Mon 16/10/23	Fri 12/01/24	[Timeline bar]											
23		VP3 construction	65 days	Mon 6/11/23	Fri 2/02/24	[Timeline bar]											
24		Rehabilitation	80 days	Mon 23/10/23	Fri 9/02/24	[Timeline bar]											
25		Hydrostatic testing	20 days	Mon 19/02/24	Fri 15/03/24	[Timeline bar]											
26		Pipeline appurtenances and valve pit fit out	65 days	Mon 18/03/24	Fri 14/06/24	[Timeline bar]											
27		Removal of stockpile yards and temporary access roads	65 days	Mon 18/03/24	Fri 14/06/24	[Timeline bar]											
28		Final rehabilitation	30 days	Mon 17/06/24	Fri 26/07/24	[Timeline bar]											
29		Pipeline Construction - VP3 to VP4	421 days	Mon 19/06/23	Mon 27/01/25	[Timeline bar]											
30		Clearing and grubbing	45 days	Mon 19/06/23	Fri 18/08/23	[Timeline bar]											
31		Access track construction	45 days	Mon 21/08/23	Fri 20/10/23	[Timeline bar]											
32		Dig, lay and backfill pipe	120 days	Mon 23/10/23	Fri 5/04/24	[Timeline bar]											
33		Barratta Ck and Horsecamp Ck crossing	90 days	Mon 8/04/24	Fri 9/08/24	[Timeline bar]											
34		TB4 construction	65 days	Mon 23/10/23	Fri 19/01/24	[Timeline bar]											
35		TB5 construction	65 days	Mon 4/12/23	Fri 1/03/24	[Timeline bar]											
36		TB6 construction	65 days	Mon 1/01/24	Fri 29/03/24	[Timeline bar]											
37		VP4 construction	65 days	Mon 29/01/24	Fri 26/04/24	[Timeline bar]											
38		Rehabilitation	190 days	Mon 20/11/23	Fri 9/08/24	[Timeline bar]											
39		Hydrostatic testing	20 days	Tue 20/08/24	Mon 16/09/24	[Timeline bar]											
40		Pipeline appurtenances and valve pit fit out	65 days	Tue 17/09/24	Mon 16/12/24	[Timeline bar]											
41		Removal of stockpile yards and temporary access roads	65 days	Tue 17/09/24	Mon 16/12/24	[Timeline bar]											
42		Final rehabilitation	30 days	Tue 17/12/24	Mon 27/01/25	[Timeline bar]											
43		Pipeline Construction Section 4 - VP4 to Stage 1.1b Connection	400 days	Mon 15/05/23	Fri 22/11/24	[Timeline bar]											

Date: Tue 18/10/22


Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Manual Progress
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Gantt Chart (Timeline from Half 1, 2023 to Half 2, 2026)											
44		Clearing and grubbing	35 days	Mon 15/05/23	Fri 30/06/23	[Gantt bar]											
45		Access track construction	25 days	Mon 3/07/23	Fri 4/08/23	[Gantt bar]											
46		Oaky Ck crossing	50 days	Mon 7/08/23	Fri 13/10/23	[Gantt bar]											
47		Dig, lay and backfill pipe	175 days	Mon 16/10/23	Fri 14/06/24	[Gantt bar]											
48		TB7 construction	50 days	Mon 7/08/23	Fri 13/10/23	[Gantt bar]											
49		TB8 construction	50 days	Mon 28/08/23	Fri 3/11/23	[Gantt bar]											
50		TB9 construction	50 days	Mon 18/09/23	Fri 24/11/23	[Gantt bar]											
51		TB10 construction	50 days	Mon 9/10/23	Fri 15/12/23	[Gantt bar]											
52		TB11 construction	50 days	Mon 30/10/23	Fri 5/01/24	[Gantt bar]											
53		Private Landowner 3 irrigation siphon	50 days	Mon 11/12/23	Fri 16/02/24	[Gantt bar]											
54		Rehabilitation	155 days	Mon 13/11/23	Fri 14/06/24	[Gantt bar]											
55		Hydrostatic testing	20 days	Mon 17/06/24	Fri 12/07/24	[Gantt bar]											
56		Pipeline appurtenances and valve pit fit out	65 days	Mon 15/07/24	Fri 11/10/24	[Gantt bar]											
57		Removal of stockpile yards and temporary access roads	65 days	Mon 15/07/24	Fri 11/10/24	[Gantt bar]											
58		Final rehabilitation	30 days	Mon 14/10/24	Fri 22/11/24	[Gantt bar]											
59		Pipeline Completion and Handover	281 days	Tue 28/01/25	Tue 24/02/26	[Milestone bar]											
60		Demobilise	20 days	Tue 28/01/25	Mon 24/02/25	[Gantt bar]											
61		Practical completion	0 days	Mon 24/02/25	Mon 24/02/25	[Milestone diamond]											
62		12 months defects liability period	261 days	Tue 25/02/25	Tue 24/02/26	[Gantt bar]											
63		Project completion	0 days	Tue 24/02/26	Tue 24/02/26	[Milestone diamond]											
64		TCW00423 TRENCHLESS CONSTRUCTION	596 days	Mon 3/04/23	Mon 14/07/25	[Milestone bar]											
65		Possession of site	0 days	Mon 3/04/23	Mon 3/04/23	[Milestone diamond]											
66		Ayr Dalbeg Road / Wilmar Cane Rail Track	90 days	Mon 3/04/23	Fri 4/08/23	[Milestone bar]											
67		Site mobilisation and establishment	10 days	Mon 3/04/23	Fri 14/04/23	[Gantt bar]											
68		Launch shaft construction	25 days	Mon 17/04/23	Fri 19/05/23	[Gantt bar]											
69		Receival shaft construction	25 days	Mon 17/04/23	Fri 19/05/23	[Gantt bar]											
70		Enveloper construction and installation	15 days	Mon 22/05/23	Fri 9/06/23	[Gantt bar]											
71		Hydrostatic testing	5 days	Mon 12/06/23	Fri 16/06/23	[Gantt bar]											
72		MSCCL construction and completion	30 days	Mon 19/06/23	Fri 28/07/23	[Gantt bar]											
73		Demobilisation	5 days	Mon 31/07/23	Fri 4/08/23	[Gantt bar]											
74		Sunwater Siphons BMC & BA1	165 days	Mon 3/04/23	Fri 17/11/23	[Milestone bar]											
75		Site mobilisation and establishment	5 days	Mon 3/04/23	Fri 7/04/23	[Gantt bar]											
76		Launch shaft construction	50 days	Mon 10/04/23	Fri 16/06/23	[Gantt bar]											
77		Receival shaft construction	50 days	Mon 10/04/23	Fri 16/06/23	[Gantt bar]											
78		Enveloper construction and installation	50 days	Mon 19/06/23	Fri 25/08/23	[Gantt bar]											
79		Hydrostatic testing	5 days	Mon 28/08/23	Fri 1/09/23	[Gantt bar]											
80		MSCCL construction and completion	50 days	Mon 4/09/23	Fri 10/11/23	[Gantt bar]											
81		Demobilisation	5 days	Mon 13/11/23	Fri 17/11/23	[Gantt bar]											
82		Scott Creek	205 days	Mon 3/04/23	Fri 12/01/24	[Milestone bar]											
83		Site mobilisation and establishment	35 days	Mon 3/04/23	Fri 19/05/23	[Gantt bar]											
84		Launch shaft construction	50 days	Mon 10/07/23	Fri 15/09/23	[Gantt bar]											
85		Receival shaft construction	50 days	Mon 10/07/23	Fri 15/09/23	[Gantt bar]											
86		Enveloper construction and installation	50 days	Mon 18/09/23	Fri 24/11/23	[Gantt bar]											

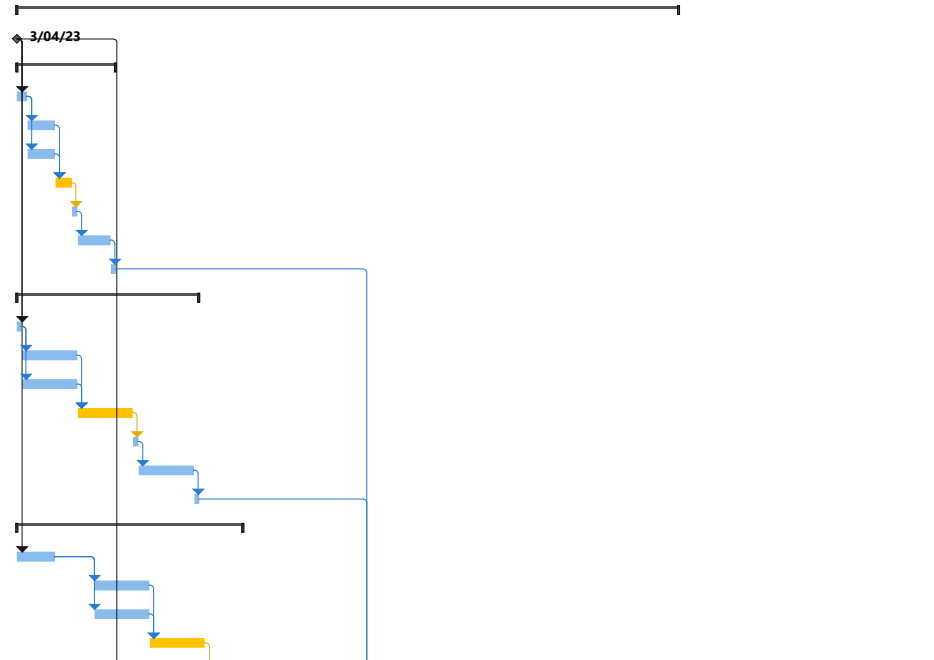

Date: Tue 18/10/22

Task	Summary	Inactive Milestone	Milestone	Duration-only	Start-only	External Milestone	Manual Progress
Split	Project Summary	Inactive Summary	Manual Task	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Progress	Progress	Progress

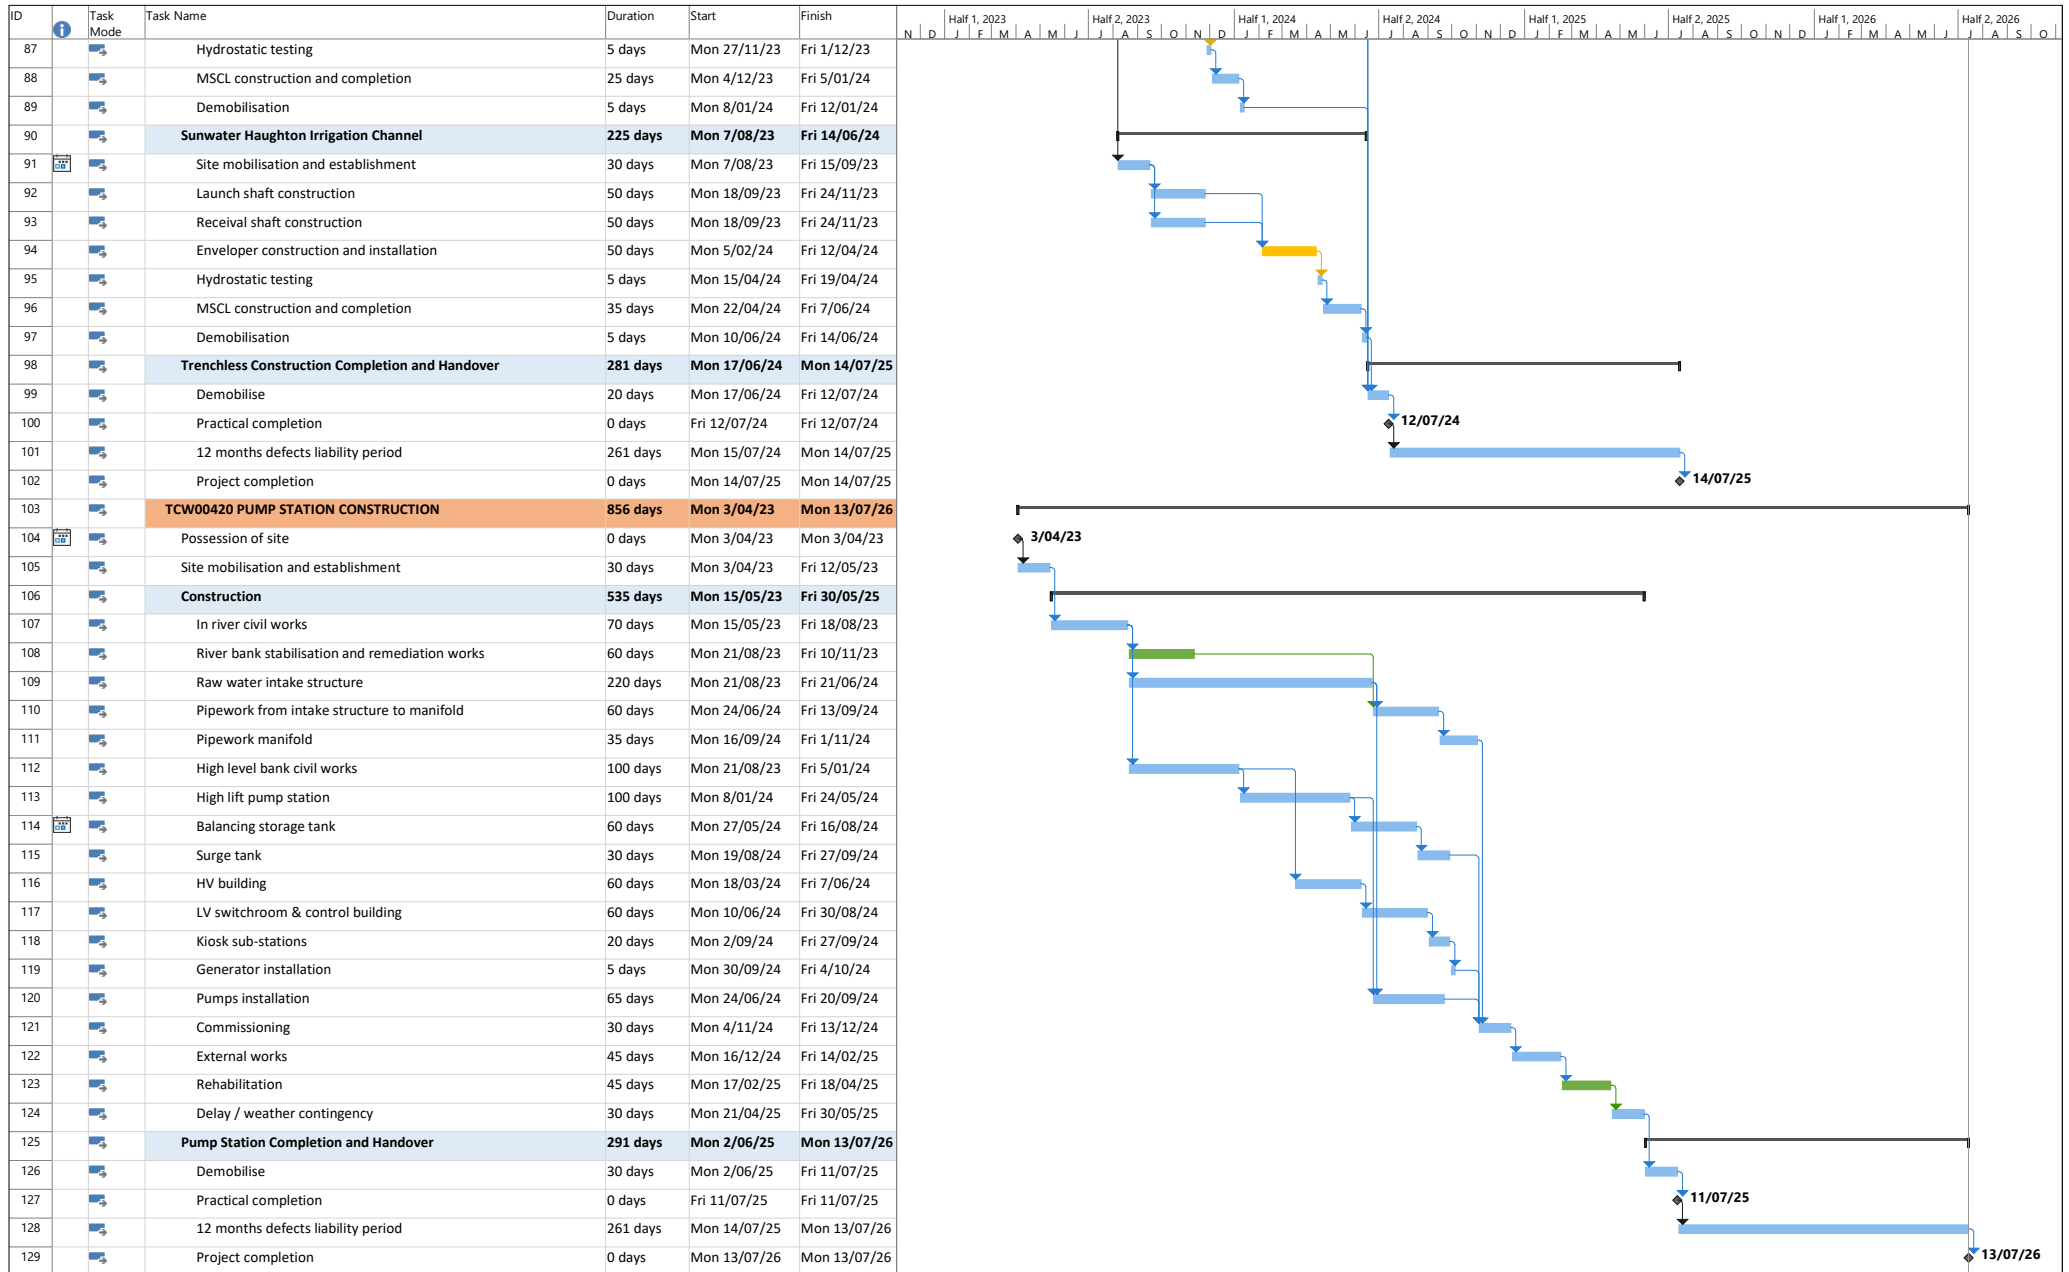

Date: Tue 18/10/22

Task		Summary		Inactive Milestone		Duration-only		Start-only		Finish-only		External Milestone		Manual Progress
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Start-only		Finish-only		External Milestone		Manual Progress
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress				
